Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish
FINANCIAL PROCESS						
2490	QPR - PEAB Phase 2 - Submit MFP to HUD	0	0	100		05APR07A
2500	QPR - PEAB Phase 2 - Submit Evident's to HUD	0	0	100		02MAY07A
2510	QPR - PEAB Phase 2 - CLOSING	0	0	0		29JUN07*
COMMUNITY & SUPPORTIVE SERVICES						
4100	CSS Case Management	1,052	11	99	18APR03A	14JUN07
4110	Homeownerhsip Counseling Program	1,045	40	96	16JUN03A	25JUL07
DEMOLITION & SITE PREP						
7210	PEAB Phase 2 - Site Remediation/Prep	60	0	100	01MAY07A	31MAY07A
INFRASTRUCTURE						
8570	Georgia Power - Phase 2 Primary & Street Lights	66	66	0	02AUG07	01NOV07
8580	Georgia Power - Phase 2 Distribution	66	66	0	03SEP07	03DEC07
NEW CONSTRUCTION						
10300	Homeownership - Scattered Site Homes (13)	839	150	82	27SEP04A	26DEC07
10060	Homeownership - Construction Overall Program	836*	151*	82	28SEP04A	27DEC07
10540	PEAB Phase 1 - Close-Out	66	0	100	02JAN07A	01MAY07A
10310	Wynnton - Construction 11 House Program Area 3	216	129	40	22JAN07A	27NOV07
10211	PEAB Phase 2 - Mobilize Contractor	20	0	100	26MAR07A	30MAR07A
10600	Sequence 1 - Type B2 - 8 Units	130	87	33	02APR07A	28SEP07
10610	Sequence 2 - Type B2 - 8 Units	130	87	33	02APR07A	28SEP07
10550	Block 9	152	109	28	02APR07A	30OCT07
10620	Sequence 3 - Type R2-3 - 18 Units	152	109	28	02APR07A	30OCT07
10560	Block 8	191	148	23	02APR07A	24DEC07
10630	Sequence 4 - Type Sr 3 - 63 Units	191	148	23	02APR07A	24DEC07
10640	Sequence 5 - Type TH-4-2 - 6 Units	207	164	21	02APR07A	15JAN08
10650	Sequence 6 - Type TH-4-2 - 6 Units	212	169	20	02APR07A	22JAN08
10570	Block 7	224	181	19	02APR07A	07FEB08
10660	Sequence 7 - Type R-2-3 - 18 Units	224	181	19	02APR07A	07FEB08
10670	Sequence 8 - Type R-2-3 - 18 Units	230	187	19	02APR07A	15FEB08
10680	Sequence 9 - Type TH-4-3 - 7 Units	230	187	19	02APR07A	15FEB08
10690	Sequence 10 - Type TH-4-3 - 7 Units	235	192	18	02APR07A	22FEB08
10580	Block 10	239	196	18	02APR07A	28FEB08
10700	Sequence 11 - Type R-2-3 - 18 Units	239	196	18	02APR07A	28FEB08
10710	Sequence 12 - Type TH3 - 3 Units	250	207	17	02APR07A	14MAR08
10590	Non-Block	255	212	17	02APR07A	21MAR08
10720	Sequence 13 - Type TH3 - 3 Units	255	212	17	02APR07A	21MAR08
10220	PEAB Phase 2 - Construction	260	215	17	02APR07A	26MAR08
10081	QPR - Wynnton Construction Finish	0	0	0		27NOV07*
10161	Wynnton Site - Substantial Completion Area 1	0	0	0		27NOV07
10065	Wynnton - 30 Day Deficiency Corrections Area 1	22	22	0	28NOV07	27DEC07
10079	Wynnton Site - Final Completion	0	0	0		27DEC07

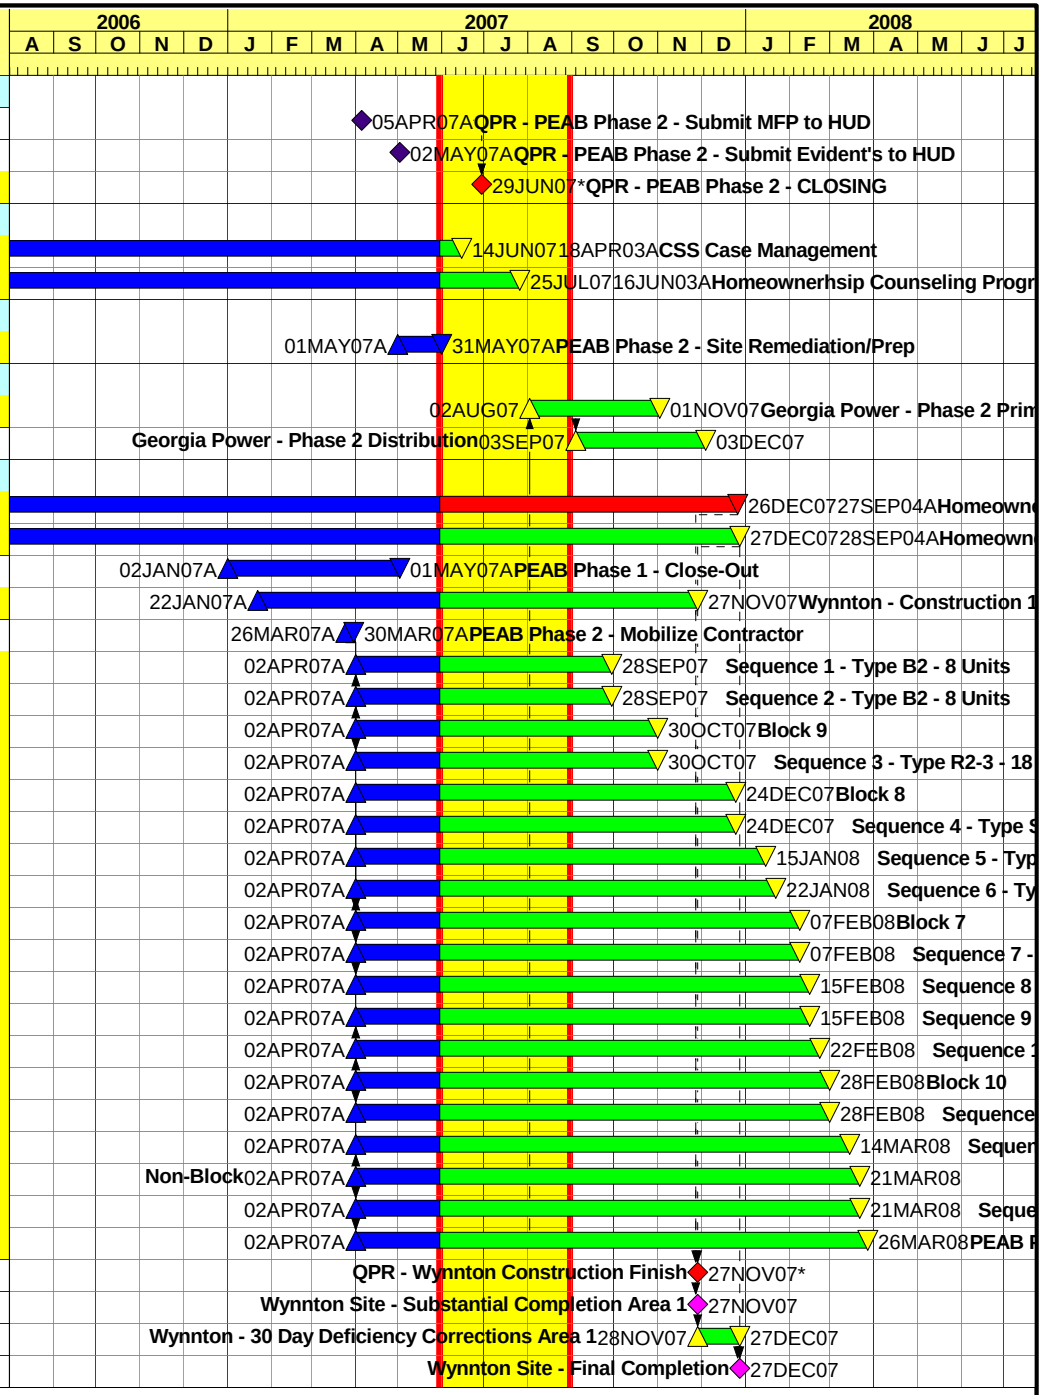

Start Date 01MAR03
Finish Date 25APR08
Data Date 31MAY07

© Primavera Systems, Inc.

Boulevard Group

Housing Authority of Columbus Georgia
PEABODY APARTMENTS HOPE VI REVITALIZATION
90 Day Lookahead Schedule

PEAB

Date	Revision	Checked	Approved
07JUN07	progress update to May 31, 2007		
